
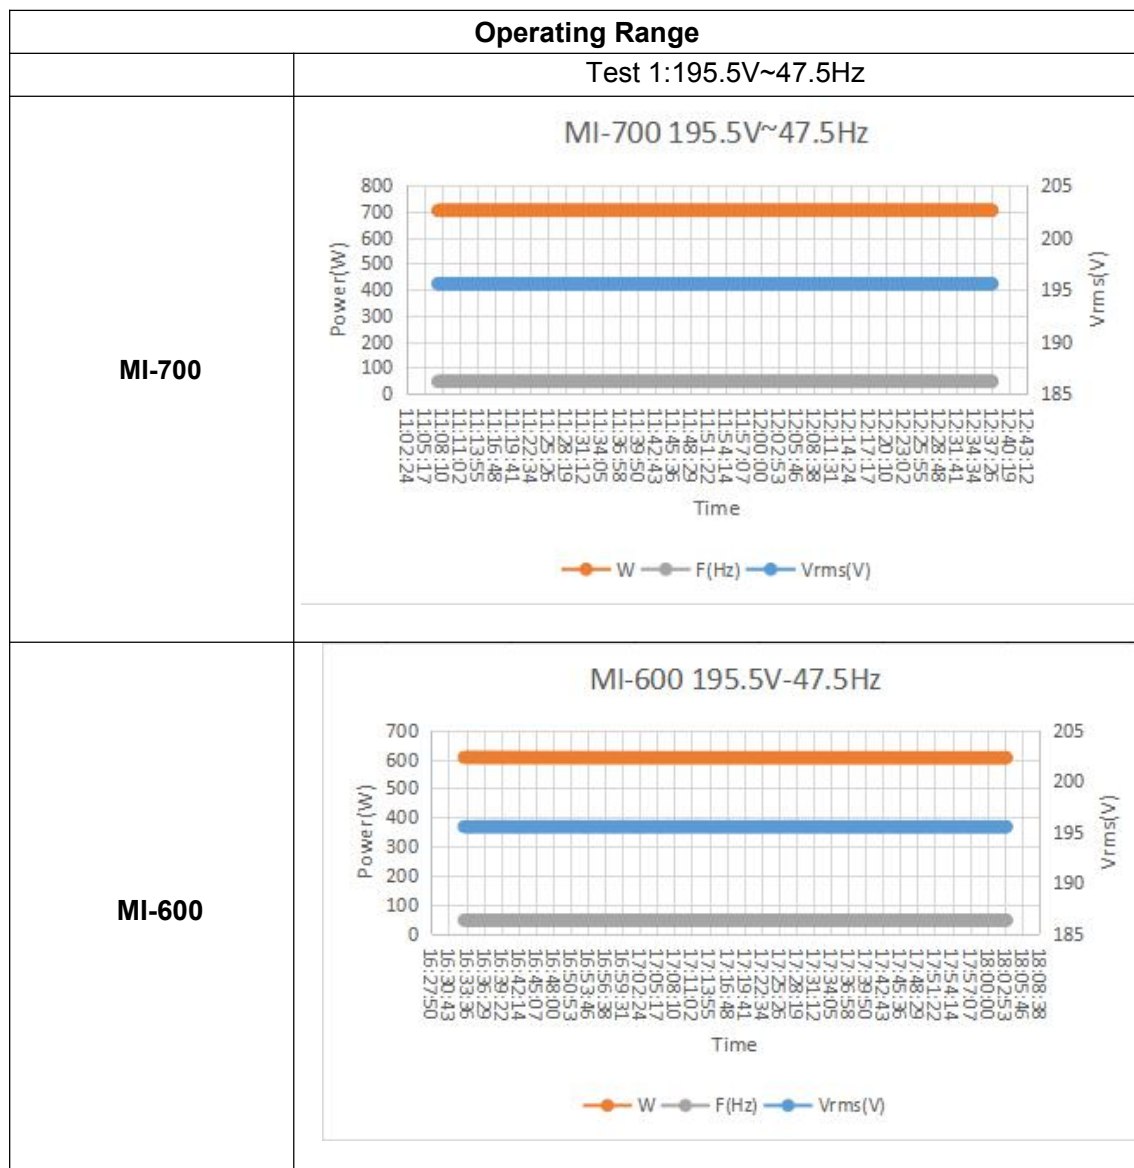


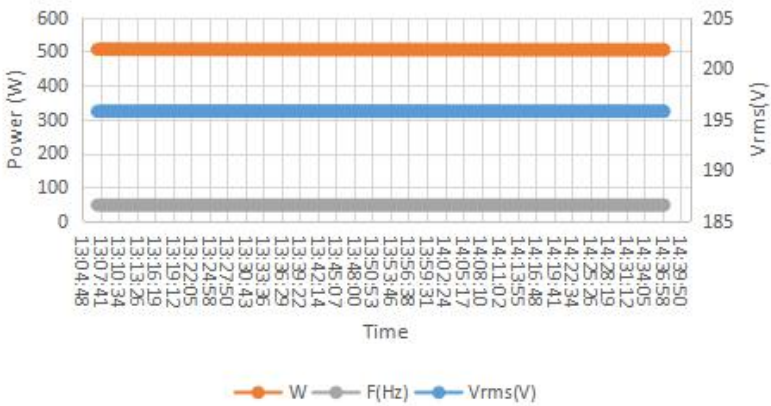
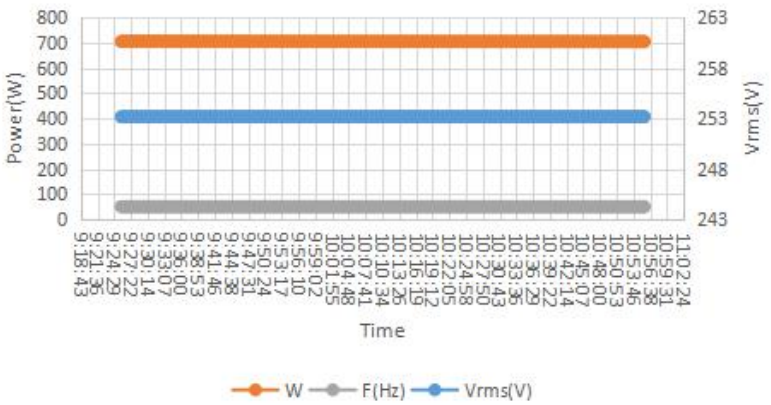
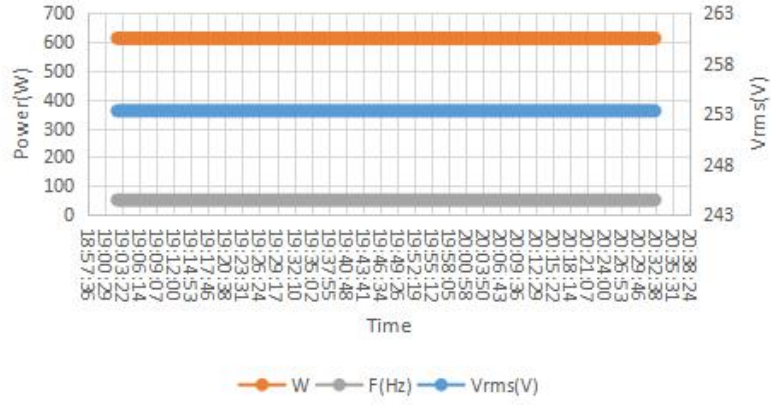
ENA EREC G98/NI:2019

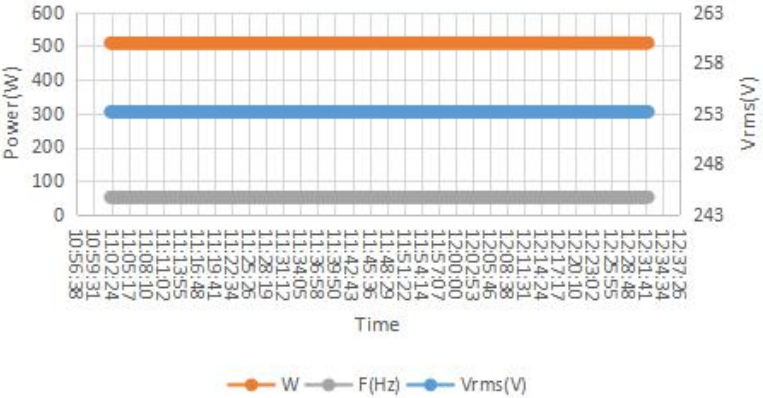
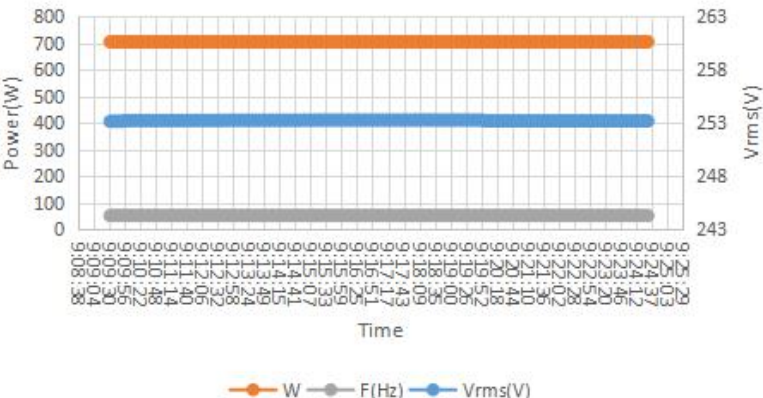
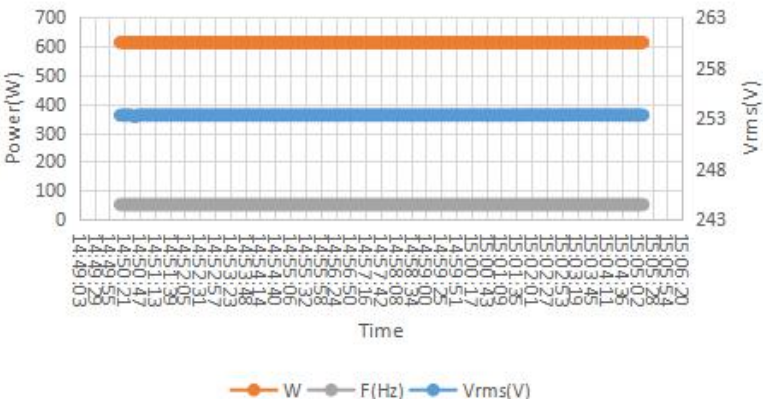
Type Approval and Manufacturer declaration of compliance with the requirements of G98/NI. This form should be used when making a Type Test submission to the Energy Networks Association (ENA). If the Micro-generator is Fully Type Tested and already registered with the ENA Type Test Verification Report Register, the Installation Document should include the Manufacturer's Reference Number (the Product ID), and this form does not need to be submitted. Where the Micro-generator is not registered with the ENA Type Test Verification Report Register this form needs to be completed and provided to the DNO, to confirm that the Microgenerator has been tested to satisfy the requirements of this EREC G98/NI.			
SSEG Type reference number		MI-700,MI-600,MI-500	
SSEG Type		Photovoltaic Microinverter	
System Supplier name		Hoymiles Converter Technology Co., Ltd.	
Address		No.18 Kangjing road, HangZhou, Zhejiang Province, P.R. China	
Tel	+86 571 28056101	Fax	+86 571 28056137
E:mail	zhangxingyao@hzconverter.com	Web site	www.hoymiles.com
Maximum rated capacity, use separate sheet if more than one connection option.	Connection Option		
	0.7/0.6/0.5	kW single phase, single, split or three phase system	
	NA	kW three phase	
	NA	kW two phases in three phase system	
	NA	kW two phases split phase system	
SSEG manufacturer/supplier declaration			
Manufacturer Type Test declaration. - I certify that all products supplied by the company with the above Type Tested reference number will be manufactured and tested to ensure that they perform as stated in this document, prior to shipment to site and that no site modifications are required to ensure that the product meets all the requirements of EREC G98/NI.			
Signed		On behalf of	Hoymiles Converter Technology Co.,Ltd

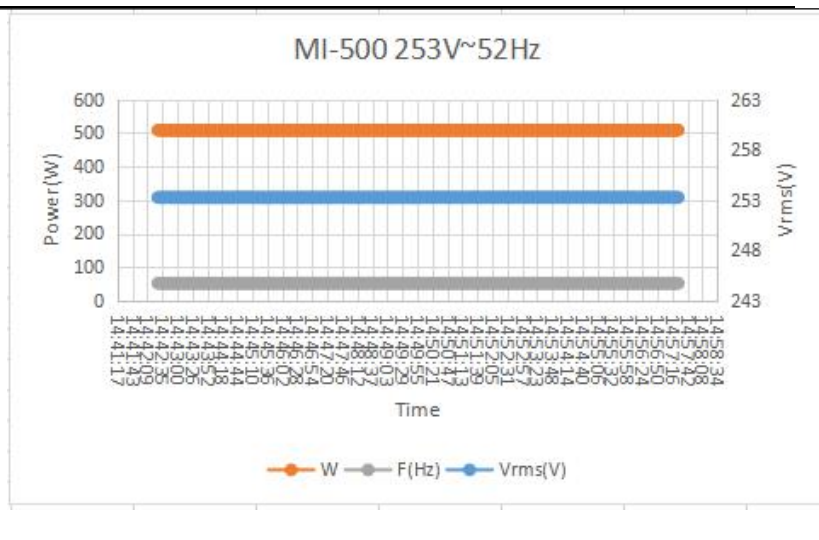
Note that testing can be done by the Manufacturer of an individual component or by an external test house.

Where parts of the testing are carried out by persons or organisations other than the Manufacturer then that person or organisation shall keep copies of all test records and results supplied to them to verify that the testing has been carried out by people with sufficient technical competency to carry out the tests.



MI-500	MI-500 195.5V~47.5Hz  Power (W) Time W F(Hz) Vrms(V)
MI-700	Test 2:253V~51.5Hz MI-700 253V~51.5Hz  Power(W) Time W F(Hz) Vrms(V)
MI-600	MI-600 253V~51.5Hz  Power(W) Time W F(Hz) Vrms(V)

MI-500	MI-500 253V~51.5Hz  Power(W) Time W F(Hz) Vrms(V)
MI-700	Test 3:253V~52Hz MI-700 253V~52Hz  Power(W) Time W F(Hz) Vrms(V)
MI-600	MI-600 253V~52Hz  Power(W) Time W F(Hz) Vrms(V)

MI-500


Power Quality – Harmonics: These tests should be carried out as specified in BS EN 61000-3-2.

SSEG rating per phase (rpp)			0.7	kW	NV=MV*3.68/rpp	
Harmo nic	At 45-55% of rated output		100% of rated output			
	Measured Value(MV) in Amps	Normalised Value (NV) In Amps	Measured Value(MV) In Amps	Normalised Value (NV) In Amps	Limit in BS EN 61000-3- 2 in Amps	Higher limit for odd harmonics 21 and above
2	0.075	0.461	0.150	0.854	1.080	
3	0.022	0.137	0.054	0.222	2.300	
4	0.012	0.072	0.029	0.070	0.430	
5	0.008	0.049	0.021	0.039	1.140	
6	0.007	0.045	0.017	0.039	0.300	
7	0.007	0.040	0.014	0.026	0.770	
8	0.006	0.034	0.012	0.021	0.230	
9	0.004	0.026	0.011	0.013	0.400	
10	0.004	0.023	0.009	0.021	0.184	
11	0.004	0.022	0.009	0.018	0.450	
12	0.004	0.021	0.008	0.015	0.153	

13	0.004	0.023	0.007	0.018	0.210	
14	0.003	0.016	0.008	0.013	0.131	
15	0.002	0.012	0.010	0.024	0.150	
16	0.002	0.012	0.006	0.008	0.115	
17	0.002	0.012	0.009	0.013	0.132	
18	0.002	0.014	0.011	0.015	0.102	
19	0.001	0.007	0.003	0.018	0.118	
20	0.001	0.004	0.004	0.013	0.092	
21	0.002	0.010	0.005	0.001	0.107	
22	0.002	0.010	0.003	0.018	0.084	
23	0.003	0.020	0.003	0.007	0.098	0.147
24	0.003	0.019	0.002	0.007	0.077	
25	0.002	0.012	0.006	0.008	0.090	0.135
26	0.002	0.012	0.003	0.001	0.071	
27	0.002	0.013	0.003	0.018	0.083	0.124
28	0.002	0.011	0.003	0.018	0.066	
29	0.002	0.015	0.003	0.014	0.078	0.117
30	0.001	0.008	0.003	0.015	0.061	
31	0.002	0.015	0.004	0.012	0.073	0.109
32	0.001	0.006	0.004	0.001	0.058	
33	0.001	0.009	0.003	0.021	0.068	0.102
34	0.001	0.004	0.003	0.007	0.054	
35	0.003	0.016	0.003	0.014	0.064	0.096
36	0.003	0.019	0.000	0.015	0.051	
37	0.002	0.011	0.003	0.005	0.061	0.091
38	0.000	0.002	0.003	0.010	0.048	
39	0.001	0.006	0.003	0.005	0.058	0.087

40	0.001	0.006	0.001	0.018	0.046	
Note the higher limits for odd harmonics 21 and above are only allowable under certain conditions, if these higher limits are utilised please state the exemption used as detailed in part 6.2.3.4 of BS EN 61000-3-2 in the box below.						

Power Quality. Voltage fluctuations and Flicker.								
	Starting			Stopping			Running	
	dmax [%]	dc [%]	d(t) [%]	dmax [%]	dc [%]	d(t) [%]	Pst	Plt 2 hours
Measured Values	0.36	0.3	0	0.36	0.3	0	0.133	0.058
Normalised to standard impedance and 3.68kW for multiple units	2.21	1.84	0	2.21	1.84	0	0.82	0.36
Limits set under BS EN 61000-3-2	4%	3.30%	3.3% 500ms	4%	3.30%	3.3% 500ms	1	0.65
Test Impedance	R	0.4	Ω	X	0.25	Ω		
Standard Impedance	R	0.24 * 0.4 ^	Ω	X	0.15 * 0.25 ^	Ω		
Maximum Impedance	R	0.4	Ω	X	0.25	Ω		

*Applies to three phase and split single phase Micro-generators.

^ Applies to single phase Micro-generators and Micro-generators using two phases on a three phase system.

For voltage change and flicker measurements the following formula is to be used to convert the measured values to the normalised values where the power factor of the generation output is 0.98 or above.

Normalised value = Measured value*reference source resistance/measured source resistance at test point.

Single phase units reference source resistance is 0.4 Ω

Two phase units in a three phase system reference source resistance is 0.4 Ω .

Two phase units in a split phase system reference source resistance is 0.24 Ω .

Three phase units reference source resistance is 0.24 Ω .

Where the power factor of the output is under 0.98 then the X to R ratio of the test impedance should be close to that of the Standard Impedance.

The stopping test should be a trip from full load operation.

The duration of these tests need to conform to the particular requirements set out in the testing notes for the technology under test. Dates and location of the test need to be noted below.

Test start date	2017-08-20	Test end date	2017-08-20
Test location	No.8 Chunxin East Road, Wuxi, Jiangsu		

Power quality – DC injection: This test should be carried out in accordance with EN 50438 Annex D.3.10

Test power level	20%	50%	75%	100%	
Recorded value(mA)	0.02	0.05	0.781	2.955	
as % of rated AC	0.003%	0.003%	0.034%	0.097%	
Limit	0.25%	0.25%	0.25%	0.25%	

Power Quality – Power factor: This test shall be carried out in accordance with EN 50538 Annex D.3.4.1 but with nominal voltage -6% and +10%. Voltage to be maintained within $\pm 1.5\%$ of the stated level during the test.

	216.2V	230V	253V	
20% of Registered	0.9779	0.9739	0.9644	
50% of Registered	0.9945	0.9937	0.9922	
75% of Registered	0.9963	0.9959	0.9951	

100% of Registered	0.9970	0.9967	0.9962	
Limit	>0.95	>0.95	>0.95	

Protection. Frequency tests These tests should be carried out in accordance with EN 50438 Annex D.2.4 and the notes in EREC G98/NI Annex A1 A 1.3.2 (Inverter connected) or Annex A2 A.2.2.2 (Synchronous)

Function	Setting		Trip test		"No trip tests"	
	Frequency	Time delay	Frequency	Time delay	Frequency /time	Confirm no trip
U/F	48Hz	0.5s	48Hz	0.53s	48.2Hz/ 25s	Confirm
					47.8Hz/ 0.45s	Confirm
O/F	52Hz	1.0s	52Hz	1.04s	51.8Hz/120s	Confirm
					52.2Hz/ 0.98s	Confirm

Protection. Voltage tests These tests should be carried out in accordance with EN 50438 Annex D.2.3 and the notes in EREC G98/NI Annex A1 A 1.3.1 (Inverter connected) or Annex A2 A.2.2.1 (Synchronous)

Function	Setting		Trip test		"No trip tests"	
	Voltage	Time delay	Voltage	Time delay	Voltage /time	Confirm no trip
U/V stage 1	195.5V	3.0s	195.8V	3.06s	199.5V/5.0s	Confirm
U/V stage 2	138V	2.0s	137.7V	2.03s	142V/2.5s	Confirm
					134V/1.95s	Confirm
O/V stage 1	253V	0.5s	252.9V	0.52s	249V/5.0s	Confirm
					257V/0.45s	Confirm

Note for Voltage tests the Voltage required to trip is the setting ± 3.45 V. The time delay can be measured at a larger deviation than the minimum required to operate the protection. The No trip tests need to be carried out at the setting ± 4 V and for the relevant times as shown in the table above to ensure that the protection will not trip in error.

Protection. Loss of Mains test. For PV Inverters shall be tested in accordance with BS EN62116. Other Inverters should be tested in accordance with EN 50438 Annex D.2.5 at 10%,55% and 100% of rated power.

Note: Inverter tested according to BS EN 62116.

Test Power and imbalance	33% -5% Q	66% -5% Q	100% -5% P	33% +5% Q	66% +5% Q	100% +5% P
Trip time. Limit is 0.5s	19.07ms	427.1ms	435.1ms	21.47ms	413.5ms	429.5ms

Protection. Frequency change, Stability test This test should be carried out in accordance with EREC G98/NI Annex A1 A 1.3.5 (Inverter connected) or Annex A2 A.2.2.5 (Synchronous).

	Start Frequency	Change	End Frequency	Confirm no trip
Positive Vector Shift	49.5Hz	+50 degrees		Confirm
Negative Vector Shift	50.5Hz	- 50degrees		Confirm

Protection – Frequency change, RoCoF Stability test: The requirement is specified in section 11.3, test procedure in Annex A 1.3.5 (Inverter connected) or Annex A2 A.2.2.5 (Synchronous).

	Ramp range	Test frequency	Test Duration	Confirm no trip
Positive Frequency drift	49Hz to 51Hz	+0.95Hz/sec	2.1s	Confirm
Negative Frequency drift	51Hz to 49Hz	-0.95Hz/sec	2.1s	Confirm

Protection – Limited Frequency Sensitive Mode – Overfrequency test: This test should be carried out in accordance with EN 50438 Annex D.3.3 Power response to over- frequency. The test should be carried out using the specific threshold frequency of 50.4 Hz and dro op of 10%.

Test sequence at Registered Capacity >80%	Measured Active Power Output	Frequency	Primary Power Source	Active Power Gradient
Step a) 50.00 Hz ± 0.01 Hz	700W	50Hz		-
Step b) 50.45 Hz ± 0.05 Hz	693.2W	50.45Hz		-
Step c) 50.70 Hz ± 0.10 Hz	658.8W	50.7Hz		-
Step d) 51.15 Hz ± 0.05 Hz	597.5W	51.15Hz		-
Step e) 50.70 Hz ± 0.10 Hz	659.0W	50.7Hz		-

Step f) 50.45 Hz ±0.05Hz	693.3W	50.45Hz		-
Step g) 50.00 Hz ±0.10Hz	700.1W	50Hz		-
Test sequence at Registered Capacity 40% - 60%	Measured Active Power Output	Frequency	Primary Power Source	Active Power Gradient
Step a) 50.00 Hz ±0.01Hz	352.5W	50Hz		-
Step b) 50.45 Hz ±0.05Hz	348.9W	50.45Hz		-
Step c) 50.70 Hz ±0.10Hz	332.1W	50.7Hz		-
Step d) 51.15 Hz ±0.05 Hz	301.2W	51.15Hz		-
Step e) 50.70 Hz ±0.10Hz	332.2W	50.7Hz		-
Step f) 50.45 Hz ±0.05Hz	349.1W	50.45Hz		-
Step g) 50.00 Hz ±0.10Hz	352.6W	50Hz		-
Steps as defined in EN 50438				

Protection – Power output with falling frequency test: This test should be carried out in accordance with EN 50438 Annex D.3.2 active power feed -in at under-frequency.

Test sequence	Measured Active Power Output	Frequency	Primary power source
Test a) 50 Hz ± 0.01 Hz	700.13W	50Hz	DC supply
Test b) Point between 49.5 Hz and 49.6 Hz	699.99W	49.55Hz	DC supply
Test c) Point between 47.5 Hz and 47.6 Hz	699.88W	47.55Hz	DC supply

NOTE: The operating point in Test (b) and (c) shall be maintained for at least 5 minutes

Protection. Re-connection timer.

Test should prove that the reconnection sequence starts after a minimum delay of 20 s for restoration of voltage and frequency to within the stage 1 settings of Table 2.

Time delay setting	Measured delay	No reconnection when voltage or frequency is brought to just outside stage 1 limits of table 1.			
60s	90s	At 257V	At 191.5V	At 47.9Hz	At 52.1Hz

Confirmation that the SSEG does not re-connect.	Confirm	Confirm	Confirm	Confirm
---	---------	---------	---------	---------

Fault level contribution. The requirement is specified in section 5.7, test procedure in Annex A or B 1.4.6

For a directly coupled SSEG			For a Inverter SSEG		
Parameter	Symbol	Value	Time after fault	Volts	Amps
Peak Short Circuit current	i_p	N/A	20ms	19.61V	0.171A
Initial Value of aperiodic	A	N/A	100ms	10.50V	0.143A
Initial symmetrical	I_k	N/A	250ms	8.56V	0.130A
Decaying (aperiodic)	i_{DC}	N/A	500ms	6.92V	0.108A
Reactance/Resistance Ratio	X/R	N/A	Time to trip	0.0024	(in seconds)

Self-Monitoring solid state switching :No specified test requirements. Refer to EREC G98/NI Annex A1 A 1.4.6 (Inverter connected).

Yes/or NA

It has been verified that in the event of the solid state switching device failing to disconnect the Micro-generator, the voltage on the output side of the switching device is reduced to a value below 50 V within 0.5 s.

N/A

Logic interface (input port)

Yes/or NA

Confirm that an input port is provided and can be used to shut down the module.

Yes

Additional comments
